

APPENDIX 15

Avenal State Prison



CALIFORNIA
PRISON HEALTH CARE
RECEIVERSHIP CORP.



Program Statistics

- **Location:**
Avenal State Prison
- **Inmate Population:**
7,525 Inmates
- **Procurement Methods:**
Design-Build
Design-Bid-Build
- **Program Stages:**
Design, Construction
and Procurement

Project Issues

Master Plan Addendum No. 1 approved the adjustment to the Program Budget and authorized the Implementation Team to move forward and proceed on all projects. An updated Implementation Plan is in development to be issued to define revised implementation strategies resulting for the additional work scope.

The Valley Fever Plan has been approved and is being instituted.

VANIR CONSTRUCTION MANAGEMENT, INC. HEALTH CARE FACILITY IMPROVEMENT PROGRAM

Project Description

The Avenal State Prison Program consists of constructing three Complex Medical Clinics, a new Modular Health Services Administration Building, new Medical Supply Warehouse, procurement and services for Eight 5th Wheel Medical Clinics, procurement and set up of a temporary administration modular, renovation to areas within the Infirmary Building 390, conversion of existing medical building 395 into a Pharmacy, expansion of pill rooms and the addition of an Ad. Seg. Clinic.

Master Plan Addendum No. 1, approved in July, 2008 added project scope to include the expansion of medical records, addition of inmate waiting at CHS specialty Bldg. 390, Nurse Call system, canopies for pill lines and central core clinic trailers as well as addition of space for the custody access team in the Admin. Bldg.



Avenal State Prison

Schedule Narrative

Additional contract time was added to the ASP-04 construction duration. This extension coupled with the addition of work scope added by Master Plan Addendum No. 1 (ASP-08), has pushed the Projected Program Completion

Completed Projects:

ASP-01a, 5th Wheel Medical Clinics—Core
ASP-01b, 5th Wheel Medical Clinics—Yards
ASP-02, Temporary Admin. & Custody Access Modulares
ASP-07, Nurse Call System

BUDGET STATUS

Original Program Budget	\$27,500,000.00
Program Budget Adjustments	\$5,929,830.00
Current Program Budget	\$33,429,830.00
Projected Program Cost	\$33,269,005.00
Encumbrances To-Date	4,277,204.98
Expended To-Date	\$1,928,433.40

SCHEDULE STATUS

Date of Authorization to Proceed:	September 2007
Planned Program Completion Date:	Nov. 2009
Projected Program Completion Date:	Dec. 2009

Avenal State Prison



Project Statistics

- **Location:**
Avenal State Prison
- **Project Name**
ASP-01a: 5th Wheel Medical Clinics, Core
- **Vanir CM Representative**
Kimberly Bobic
- **Supplier**
K&D
- **Procurement Method**
Bid-Build
- **Project Stage**
Complete

VANIR CONSTRUCTION MANAGEMENT, INC. 5TH WHEEL MEDICAL CLINICS, CORE ASP-01A

Project Description

Provide and install two (2) 5th wheel Medical trailer clinics located in front of Building #395 and across from Building #390, the Central Health Services Building. The two trailers provide (4) new clinical exam rooms and (2) rest-rooms for use by the institution for both general clinic and specialty exam. The two trailers shall have a connecting deck and ramp for access and inmate waiting.



West view of fully operational 5th Wheel Medical clinic

Project Issues

Both 5th wheel medical clinics located in front of building #395 are complete and are fully operational.

Awaiting final trailer connection costs from ASP Plant Operations.

Approval was given to provide a shade canopy between the trailers and over the deck. Design for the canopy was included in the MP Addendum.

Schedule Narrative

Procurement:

July 9, 2007 -
October 19, 2007

Delivery:

October 31, 2007

Hook-up & Occupancy

October 31 —
November 13, 2007

Duration:

Four (4) months

BUDGET STATUS

Current Project Budget:	\$470,000.00
Current Construction Budget:	\$400,000.00
Actual Construction Contract Amount:	\$374,860.00
Change Orders Approved to Date:	\$0.00
Change Orders Pending:	\$0.00
Change Orders Projected:	\$30,000.00
Projected Construction Contract Cost:	\$404,860.00
Construction Contract Paid to Date:	\$374,860.00
Projected Project Budget:	\$470,000.00
Total Encumbrance:	\$374,800.00
Paid to Date:	\$374,860.00

SCHEDULE STATUS

Project is Complete

Date of Procurement:	July 9, 2007
Current Project Completion Date:	November 13, 2007
Projected Project Completion Date:	November 13, 2007
Project Occupancy:	November 13, 2007

* Canopy approved by Master Plan Addendum No. 1 to be procured concurrent with ASP-05, Clinic Pill Canopies and encumbered against this contract.

Avenal State Prison



CALIFORNIA
PRISON HEALTH CARE
RECEIVERSHIP CORP.



Project Statistics

- **Location:**
Avenal State Prison
- **Project Name**
ASP-01b: 5th Wheel
Medical Clinics, Facility
- **Vanir CM Representative**
Scott Murphy
- **Supplier**
American Custom
Coach
- **Procurement Method**
Bid-Build
- **Project Stage**
Complete

Project Issues

All six 5th wheel medical trailer clinics have been delivered, set-up and turned over to the facility for their intended use.

VANIR CONSTRUCTION MANAGEMENT, INC. 5TH WHEEL MEDICAL CLINICS, FACILITY- ASP-01B

Project Description

Provide and install six (6) 5th wheel Medical trailer clinics, installing one (1) trailer clinic at each of the six facility yard clinics. Each trailer consists of two (2) exam rooms, work-space, and one restroom that will temporarily supplement the existing medical space within the existing clinic until which time the new complex facility clinic can be constructed and occupied. Each trailer has ADA compliant ramping and perimeter fencing with two man-gates.

Schedule Narrative

Procurement:

December 1, 2007 -
January 30, 2008

Delivery:

February 22, 2008 -
July 31, 2008

Hook-up & Occupancy

April 9 - August, 2008

Duration:

Eight (8) months



North View of Facility One 5th Wheel Medical Clinic

BUDGET STATUS

Current Project Budget:	\$1,410,000.00
Current Construction Budget:	\$1,200,000.00
Actual Construction Contract Amount:	\$1,197,989.80
Change Orders Approved to Date:	\$5,910.00
Change Orders Pending:	\$0.00
Change Orders Projected:	\$0.00
Projected Construction Contract Cost:	\$1,203,899.80
Construction Contract Paid to Date:	\$1,109,451.31
Projected Project Budget:	\$1,215,000.00
Total Encumbrance:	\$1,203,899.80
Paid to Date:	\$1,109,451.31

SCHEDULE STATUS

Project is Complete

Date of Notice to Proceed:	December 1, 2007
Current Project Completion Date:	August 31, 2008
Projected Project Completion Date:	August 31, 2008
Project Occupancy:	September 3, 2008

Avenal State Prison



CALIFORNIA
PRISON HEALTH CARE
RECEIVERSHIP CORP.



Project Statistics

- **Location:**
Avenal State Prison
- **Project Name**
ASP-02: Temporary Administration & Health Care Custody Access Modulares
- **Vanir CM Representative**
Scott Murphy
- **Supplier**
Pacific Mobile
- **Procurement Method**
Bid-Build
- **Project Stage**
Complete

Project Issues

Temporary Admin. Modular is complete.

Additional work added to the project by Master Plan Addendum No. 1 includes the 24'x60' Custody Access Trailer, as well as the addition of phone, data and new lighting in the existing transportation office/ future Dental Administration office.

VCM has requested quotes to provide baserock at an adjacent pad for the 16 transportation vans use.

VANIR CONSTRUCTION MANAGEMENT, INC. TEMPORARY ADMINISTRATION & HEALTH CARE CUSTODY ACCESS MODULARS – ASP-02

Project Description

Lease and install a double-wide modular building for temporary location of administration staff from Building #390 to allow re-assignment as specialty exam rooms and clinical support functions and Building #395 to facilitate its renovation for Pharmacy. Space to accommodate six (6) supervising RNs and three (3) scheduling staff consisting of seven (7) offices, two rest-rooms and a meeting area. The modular unit shall be located next to Building 495.

Schedule Narrative

Procurement:

January 22, 2008 -March 28, 2008

Delivery:

April 21, 2008

Hook-up & Occupancy

April 22 - June 18, 2008

Duration:

Six (6) months. Increased due to additional work related to Custody Access Modular



East View of the new Temporary Administration Modular

BUDGET STATUS

Current Project Budget:	\$159,725.00
Current Construction Budget:	\$150,000.00
Actual Construction Contract Amount:	\$94,533.62
Change Orders Approved to Date:	\$135,960.77
Change Orders Pending:	\$0.00
Change Orders Projected:	\$0.00
Projected Construction Contract Cost::	\$235,000.00
Construction Contract Paid to Date:	\$43,155.26
Projected Project Budget:	\$242,000.00
Total Encumbrance:	\$230,494.39
Paid to Date:	\$43,155.26

SCHEDULE STATUS

Project is substantially complete

Date of Procurement:	March 28, 2008
Current Project Completion Date:	June 17, 2008
Projected Project Completion Date:	June 17, 2008
Project Occupancy (Temp. Admin.)	June 18, 2008
(Custody Access)	August , 2008

Avenal State Prison



CALIFORNIA
PRISON HEALTH CARE
RECEIVERSHIP CORP.



Project Statistics

- **Location:**
Avenal State Prison
- **Project Name**
ASP-03: Infirmary Conversion and Pharmacy
- **Vanir CM Representative**
Darrell Chan
- **Contractor**
JTS Construction
- **Procurement Method**
Design-Bid-Build
- **Project Stage**
Construction

Project Issues

JTS Construction was issued the Notice to Proceed on August 11, 2008.

Current procurement delays of the new Pharmacy furniture for 395 has impacted the completion schedule for building 390 due to the inability to move the Pharmacy staff into their new space. Once the new Pharmacy furniture is complete in 395, JTS will be able to complete the remaining work in 390.

VANIR CONSTRUCTION MANAGEMENT, INC. INFIRMARY CONVERSION AND PHARMACY- ASP-03

Project Description

The areas to receive modification under this project are located within the existing 16,200 sf Central Health Services Building #390 and the 1,500 sf Building #395.

Work in Building #390 includes multiple areas of remodel and modification to support effective delivery of specialty health services to the inmate population of ASP.

Building #395 will be renovated for conversion into an adequately sized Pharmacy and organization to support current filling of medication prescriptions and the future use of Maxor's Guardian medication system.



Infirmary Building 390

Schedule Narrative

Construction began in August 2008.

The construction duration of the project is scheduled for four (4) months and is currently delayed due to untimely procurement of the new Pharmacy furniture. The new projected completion date is March 31, 2009.



Building 395; Future Pharmacy

BUDGET STATUS

Current Project Budget:	\$677,113.00
Current Construction Budget:	\$575,000.00
Actual Construction Contract Amount:	\$397,500.00
Change Orders Approved to Date:	\$11,726.00
Change Orders Pending:	\$(465.00)
Change Orders Projected:	\$0.00
Projected Construction Contract Cost:	\$575,000.00
Construction Contract Paid to Date:	\$64,440.00
Projected Project Budget:	\$636,813.00
Total Encumbrance:	\$408,761.00
Paid to Date:	\$64,440.00

SCHEDULE STATUS

Project is in the Contract Award Phase:

Date of Notice to Proceed:	08/11/08
Current Project Completion Date:	3/31/09
Projected Project Completion Date:	3/31/09
Project Occupancy:	Pending

Avenal State Prison



Project Statistics

- **Location:**
Avenal State Prison
- **Project Name**
ASP-04: Modular Health Services Clinics, Ad. Seg. Clinic & Administration Bldg
- **Vanir CM Representative**
Darrell Chan
- **Contractor**
JL Modular, Inc
- **Procurement Method**
Design-Build
- **Project Stage**
Construction

Project Issues

Notice to Proceed was issued to JL Modular, Inc. on December 15th, but due to the requirements that the institution be trained with regards to Valley Fever prior to any earth moving has prevented the contractor from beginning any grading or earth moving related work. The Valley Fever training for the institution is scheduled for the week of February 2nd—6th, 2009.

Valley Fever training was conducted on Feb 6th for the institution. JL Modular has begun exploratory due diligence on site and mobilization of temporary facilities and temporary fencing. Environmental consultant is on board and conducting air and dust monitoring per the requirements related to Valley Fever. Project is currently on schedule.

VANIR CONSTRUCTION MANAGEMENT, INC. MODULAR HEALTH SERVICES CLINICS, ADMINISTRATION BUILDING & AD. SEG. CLINIC – ASP-04

Project Description

The project consists of the development of three (3) new Modular Complex Clinic buildings, Ad. Seg. Clinic and a Modular Administration building.

The three Complex Clinic buildings varies in size between 6,480 and 5,760 sf each. Each shall provide medical and mental health services to each of the separate facilities contained within the complex. Each clinic will include medical exam rooms, M.H. interview rooms and group rooms and clinical staff support space. The Ad Seg. Clinic is 2,400sf and provides nurses station along with exam, interview and group rooms.

The 9,360 s.f. Administration building will be located within the secure perimeter and provide general office and support space, including a staff training room.

Schedule Narrative

The duration of the manufacturing and construction has been extended from 265 days to 365 days resulting from feedback from prospective contractors.

Contract was awarded on December 15, 2008 resetting the projected project completion date to December 15, 2009.

Project is currently on schedule.



**Location of Future Modular Health Services
Administration Building**



**North East View of Future Home to Complex
Clinic Between Facilities 3 and 4**

BUDGET STATUS

Current Project Budget:	\$18,843,115.00
Current Construction Budget:	\$15,860,100.00
Actual Construction Contract Amount:	\$13,258,500.00
Change Orders Approved to Date:	\$0.00
Change Orders Pending:	\$0.00
Change Orders Projected:	\$0.00
Projected Construction Contract Cost::	\$13,258,500.00
Construction Contract Paid to Date:	\$0.00
Projected Project Budget:	\$18,843,115.00
Total Encumbrance:	\$113,907.94
Paid to Date:	\$92,520.00

SCHEDULE STATUS

Date of Award:	12/15/08
Current Project Completion Date:	12/15/09
Projected Project Completion Date:	12/15/09
Project Occupancy:	Pending

Avenal State Prison



Project Statistics

- **Location:**
Avenal State Prison
- **Project Name**
ASP-05: Clinic Pill Canopies
- **Vanir CM Representative**
Darrell Chan
- **Contractor**
To Be Determined
- **Procurement Method**
Design-Build
- **Project Stage**
Design

Project Issues

Locations for future Pill Canopies at each yard have been identified. Development of Bid Package has begun.

This project has currently been incorporated into ASP-08.

VANIR CONSTRUCTION MANAGEMENT, INC. CLINIC PILL CANOPIES-ASP-05 (SEE ASP-08)


Project Description

The Clinic Pill Canopies were added by the Master Plan Addendum No. 1. The canopies will protect inmates waiting to receive their medication from the heat and inclement weather. Each canopy is approximately 1,400 s.f. and designed to be above the inmate accessible zone to reduce the possibility of inmates climbing on the structure. The canopy has additionally been designed with a 4:12 roof slope to allow custodial supervision beneath the structure.

Note: This bid package has been re-scoped to move the Pill Room Renovation project into ASP-08 to better align procurement methods and maximize contractor interest.

Schedule Narrative

Development of Bid Package to be completed and issued to contractors specialized in pre-engineered structures.

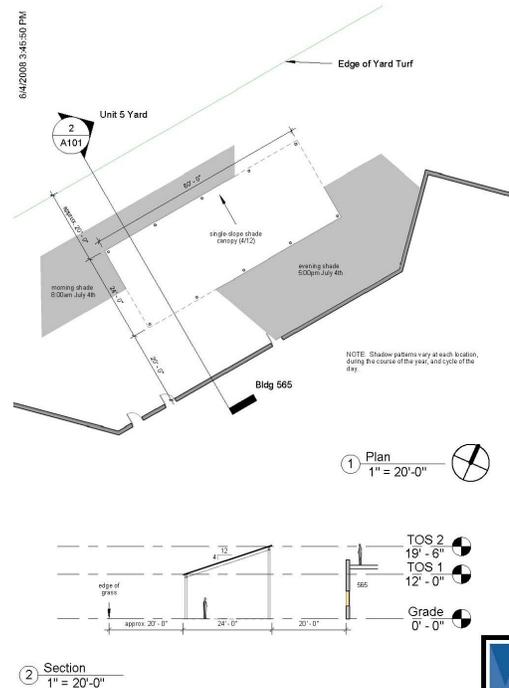

PILL LINE SHADE STRUCTURES

Pill Line Shade Structures



Health Care Facility Improvement Program
California State Prison - Avenal State Prison



BUDGET STATUS

Current Project Budget:	\$974,400.00
Current Construction Budget:	\$840,000.00
Actual Construction Contract Amount:	[Pending Award]
Change Orders Approved to Date:	\$0.00
Change Orders Pending:	\$0.00
Change Orders Projected:	\$0.00
Projected Construction Contract Cost::	\$840,000.00
Construction Contract Paid to Date:	0.00
Projected Project Budget:	\$974,000.00
Total Encumbrance:	\$22,161.00
Paid to Date:	\$19,841.00

SCHEDULE STATUS

Date of Award: [planned]	12/11/08
Current Project Completion Date:	11/19/09
Projected Project Completion Date:	11/19/09
Project Occupancy:	N/A

Avenal State Prison



CALIFORNIA
PRISON HEALTH CARE
RECEIVERSHIP CORP.



Project Statistics

- **Location:**
Avenal State Prison
- **Project Name**
ASP-06: Medical Supply Warehouse
- **Vanir CM Representative**
Darrell Chan
- **Contractor**
To Be Determined
- **Procurement Method**
Design-Build
- **Project Stage**
On-Hold

Project Issues

The Medical Supply Warehouse project ASP-06 has currently been put on hold pending funding review.

VANIR CONSTRUCTION MANAGEMENT, INC. MEDICAL SUPPLY WAREHOUSE- ASP-06

Project Description

The Project is located within the secure perimeter approximately 400 feet North of the sallyport gate. The new Medical Supply Warehouse consists of 4,000 s.f. of usable warehouse space for health services supply and equipment inventory and storage. This includes fully caged interior warehouse areas for bulk storage items, "hot" secure medical supplies and death and archive medical records. The warehouse will allow for three tier high pallet stacking of bulk supplies. The building also includes one office, workspace for four staff members, a workroom and a single unisex toilet.

Schedule Narrative

This project has currently been placed on hold. Completion of this project will be revised upon approval to proceed.



Future Location of Medical Supply Warehouse

BUDGET STATUS

Current Project Budget:	\$2,137,000.00
Current Construction Budget:	\$1,785,000.00
Actual Construction Contract Amount:	[Pending Award]
Change Orders Approved to Date:	\$0.00
Change Orders Pending:	\$0.00
Change Orders Projected:	\$0.00
Projected Construction Contract Cost::	\$1,785,000.00
Construction Contract Paid to Date:	0.00
Projected Project Budget:	\$2,137,000.00
Total Encumbrance:	\$29,500.00
Paid to Date:	\$27,1800.00

SCHEDULE STATUS

Date of Award: [Planned]	On Hold
Current Project Completion Date:	
Projected Project Completion Date:	
Project Occupancy:	Pending

Avenal State Prison



CALIFORNIA
PRISON HEALTH CARE
RECEIVERSHIP CORP.



Project Statistics

- **Location:**
Avenal State Prison
- **Project Name**
ASP-07: Nurse Call System
- **Vanir CM Representative**
Darrell Chan
- **Contractor**
Serban Sound and Communication
- **Procurement Method**
Purchase Order
- **Project Stage**
Complete

VANIR CONSTRUCTION MANAGEMENT, INC. NURSE CALL SYSTEM- ASP-07

Project Description

This project was added by the Master Plan Addendum No. 1 and installs a new Nurse Call System within the OHU of Building #390 to replace the existing inoperable system. The existing conduit pathways and infrastructure shall be re-used and a new system including cabling, devices and master station will be installed.



Existing Nurse Call Patient Panel

Project Issues

Serban Sound and communication has been awarded the project.

This project is completed.

Schedule Narrative

This project is completed pending personnel training of the new system.

BUDGET STATUS

Current Project Budget:	\$60,000.00
Current Construction Budget:	\$60,000.00
Actual Construction Contract Amount:	\$55,864.62
Change Orders Approved to Date:	\$0.00
Change Orders Pending:	\$0.00
Change Orders Projected:	\$0.00
Projected Construction Contract Cost::	\$60,000.00
Construction Contract Paid to Date:	0.00
Projected Project Budget:	\$60,000.00
Total Encumbrance:	\$55,864.62
Paid to Date:	\$0.00

SCHEDULE STATUS

Date of Award: [Planned]	06/13/08
Current Project Completion Date:	12/14/08
Projected Project Completion Date:	12/14/08
Project Occupancy:	N/A

Avenal State Prison



CALIFORNIA
PRISON HEALTH CARE
RECEIVERSHIP CORP.



Project Statistics

- **Location:**
Avenal State Prison
- **Project Name**
ASP-08: Medical Records Expansion, Inmate Waiting & Clinic Pill Room Renovation
- **Vanir CM Representative**
Darrell Chan
- **Contractor**
To Be Determined
- **Procurement Method**
Design-Bid-Build
- **Project Stage**
Design

Project Issues

Projects are currently under design.

ASP-05 Pill Canopies has been incorporated into ASP-08.

VANIR CONSTRUCTION MANAGEMENT, INC. MEDICAL RECORDS EXPANSION, INMATE WAITING, CLINIC PILL ROOM RENOVATION & PILL CANOPIES-ASP-08

Project Description

The Master Plan Addendum No. 1 added the expansion of medical records and increase of inmate waiting to the Avenal projects. The Medical Records Expansion consists of constructing a 980 s.f. addition of health records space immediately adjacent to the existing building. The addition will provide for both incoming and outgoing staging areas and sufficient staff space to allow effective record processing. The Inmate Waiting Building consists of 1,440 s.f. of space which will be constructed adjacent to Building 390 & Clinic Core exam rooms. The waiting space will provide three additional separate secure waiting areas.

This project additionally includes the expansion of the Pill Rooms in each of the current six (6) Facility Clinics to provide for two separate pill rooms with one pill administration window each to support increased and efficiency of



North View of Existing Medical Records Building

Schedule Narrative

The project is currently under design

BUDGET STATUS

Current Project Budget:	\$1,468,895.00
Current Construction Budget:	\$1,208,000.00
Actual Construction Contract Amount:	[Pending Award]
Change Orders Approved to Date:	\$0.00
Change Orders Pending:	\$0.00
Change Orders Projected:	\$0.00
Projected Construction Contract Cost:	\$1,468,895.00
Construction Contract Paid to Date:	\$0.00
Projected Project Budget:	\$1,208,000.00
Total Encumbrance:	\$22,161.00
Paid to Date:	\$18,101.00

SCHEDULE STATUS

Date of Award: [Planned]	Mar. 2009
Current Project Completion Date:	Nov. 2009
Projected Project Completion Date:	Nov. 2009
Project Occupancy:	Pending
